

# VA Southern Nevada Healthcare System



New Hospital Construction Progress May 16,  
2009



# Start of Construction



Aerial photographs of the  
New Hospital construction  
site from the cardinal  
directions.

November, 2006





# Two Years Progress

Aerial photographs of the  
New Hospital  
construction site from  
the cardinal directions.  
The Community Living  
Center is structurally  
complete.

November, 2008





April 2009





# April 2009



- Steel Decking forming first floor





- Basement level, Warehouse, CLC



# April 2009



- Basement level



# April 2009



- Community Living Center (NHCU)



# New Medical Center Complex

## Target Award Dates

**Phase 1 - Central Plant and Offsite Package**  
**Awarded: September, 2006 - Completed: April, 2008**

**Phase 2 - Foundation Package**  
**Awarded: September, 2007 - Completed: May, 2008**


**Phase 3 - Nursing Home RFP Package**  
**Awarded: September, 2007**  
**Scheduled Completion: September, 2009**

**Phase 4 - Main Hospital Package**  
**Awarded: September, 2008**  
**Scheduled Completion: September 2011**

**Activation - 6 to 12 months following construction completion**



# 4 New Primary Care Clinics

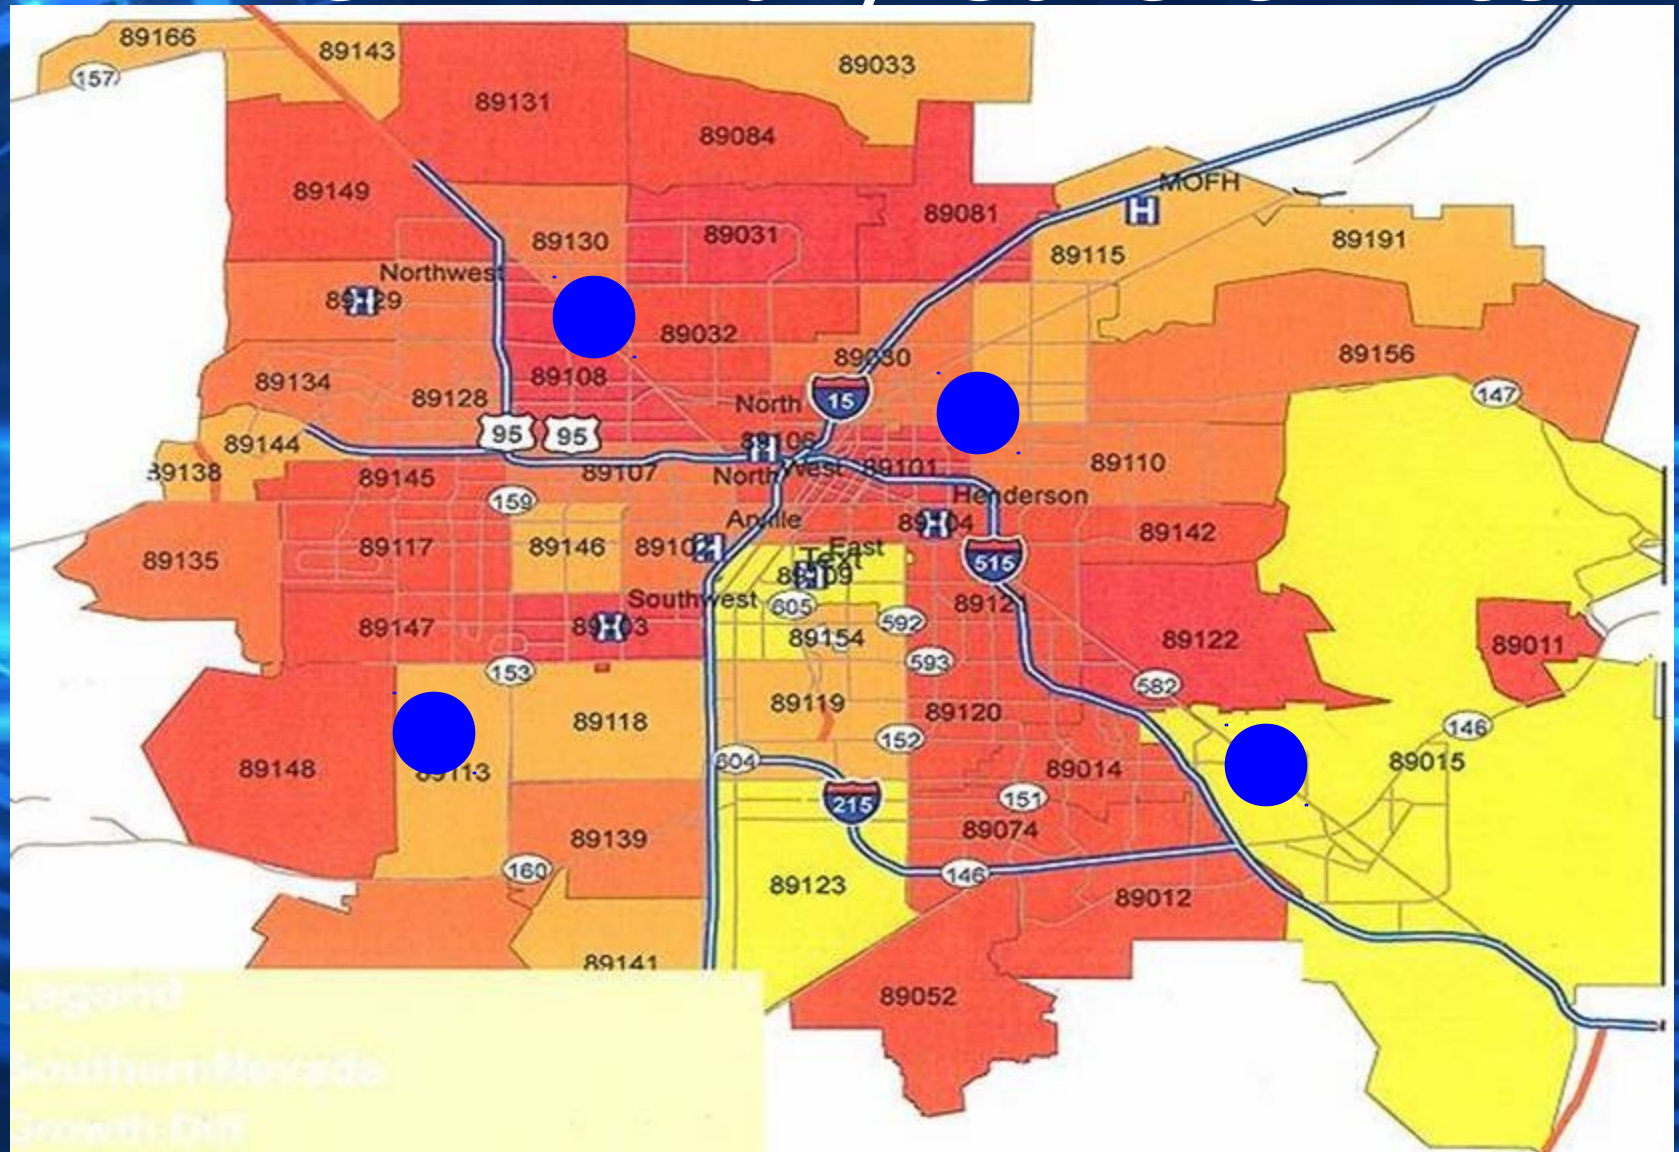

Planned Locations



# Proposed Locations

- **Southwest**
  - **Buffalo and Warm Spring**
- **Southeast**
  - **Boulder Highway and Racetrack**
- **Northwest**
  - **Rancho and Alexander**
- **Northeast**
  - **Charleston and Lamb**




# Primary Care Clinic – Artist rendering






# Primary Care Clinic (CBOC) Design

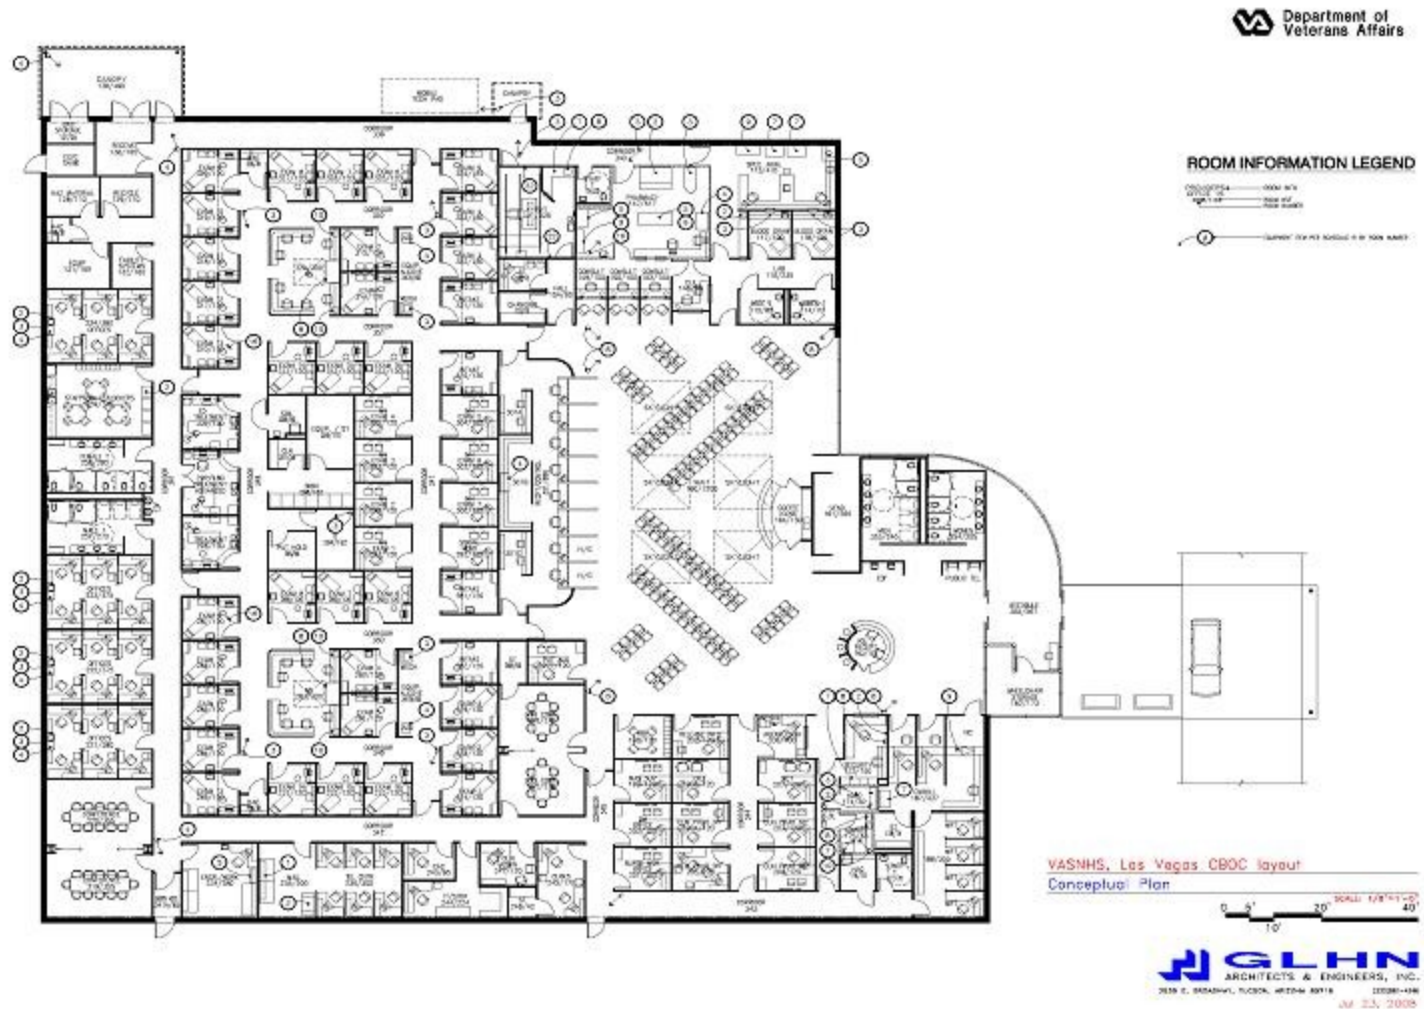

## Opening Early 2011




# Ambulatory Care Lobby

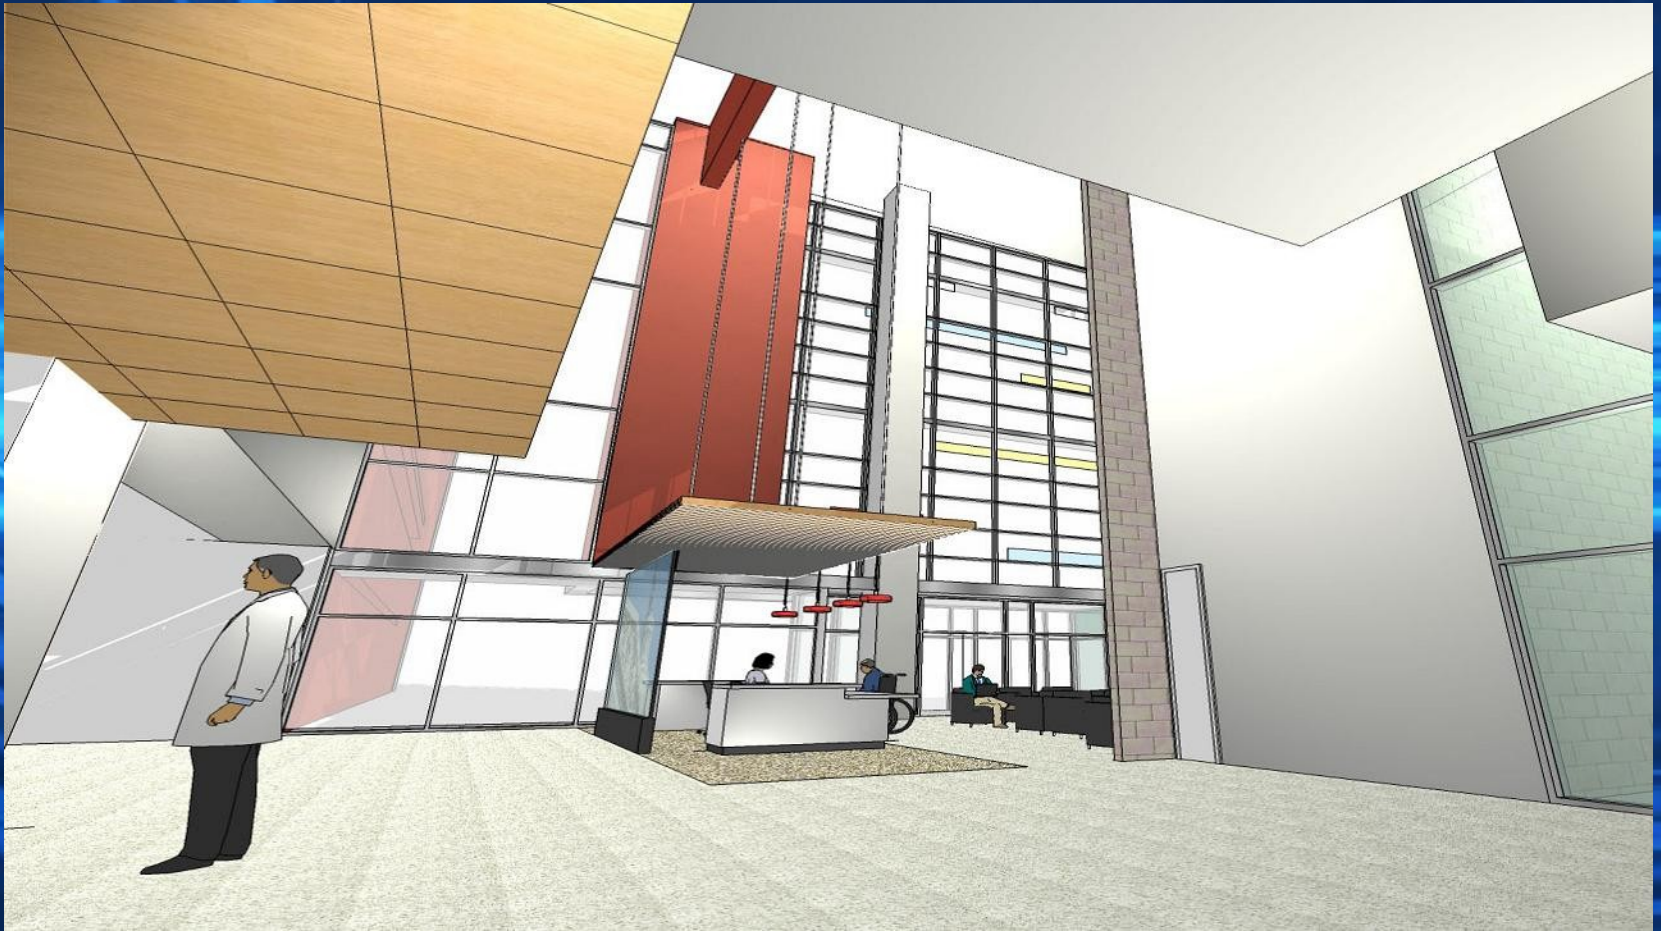



# Inpatient Room

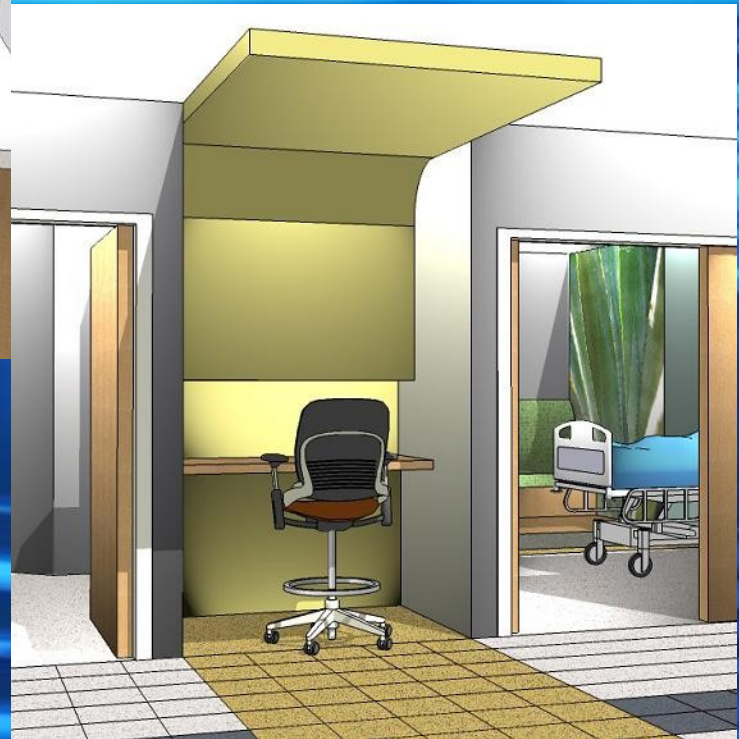



**Future Home  
of**



**VA Southern Nevada  
Health Care System**

